

Hole 7



Work already completed

Drainage exposed and rodded.

Additionally, the two parts of the drainage system had become detached along its length and was successfully reinstated.

Phase 4

Jet existing drainage.

Phase 5 – 2021-2023

Increase length of existing drainage further up the fairway.

Hole 8



Phase 3

Pond to be increased in size.

Buggy track to be laid over pond, with drainage pipes connecting both sides of pond together.

Existing connection pipe to be jetted from 16th pond.

Phase 4

Existing drains to be jetted.

Hole 9 & 10

Phase 3


Construct new manhole near 9th tee to provide jetting location point.

Phase 4

Jet existing drains.

Phase 5

New drain from area near bunkers on the 9th hole to connect to 8th pond drainage system

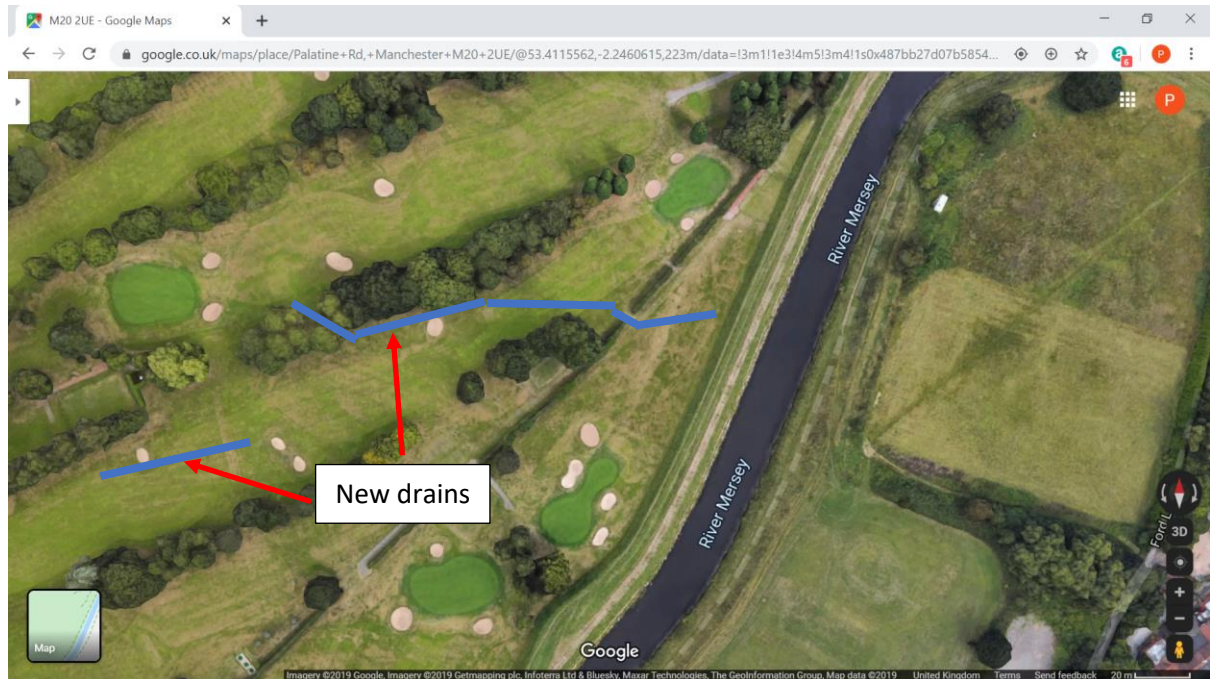

Extend land drains from the 10th hole to existing drainage on 7th, this leads into pond at 8th.

Hole 11

Work already completed has cleared blockages in the drainage.

Phase 3

Install new manhole on existing drainage run to provide easier access for jetting.



Hole 12



Phase 3

New 600mm diameter manhole to enable future jetting.

Make path to 13th longer and raise up by 200mm. This will allow additional drain from 13th to be installed.

Phase 4

Jet existing main drainage.

Phase 5

Installation of additional drains to connect to pond on 13th. (Final position to be determined).

Hole 13

Phase 3

New manhole to be installed to allow easier jetting.

Increase size of existing pond.




Phase 4

Jet from pond and new manhole position.

Phase 5 – 2021/2022

Extensions of existing fairway drains and install new additional drains to connect to manhole or pond. Final details to be confirmed.

Hole 14

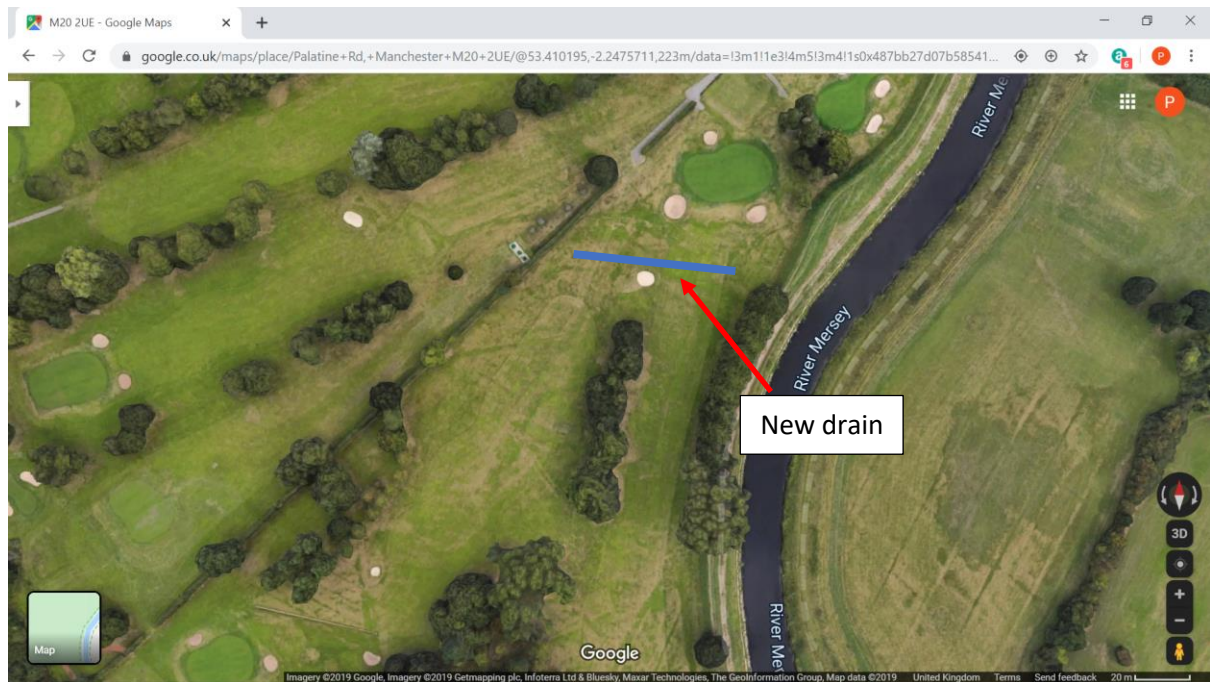


Phase 4

Existing drains in front of green to be jetted from new manhole near 11th trench.


Phase 5

Install new additional drain in front of green area.

Due to removal of trees, installation of new drain to connect to pond at 13th.

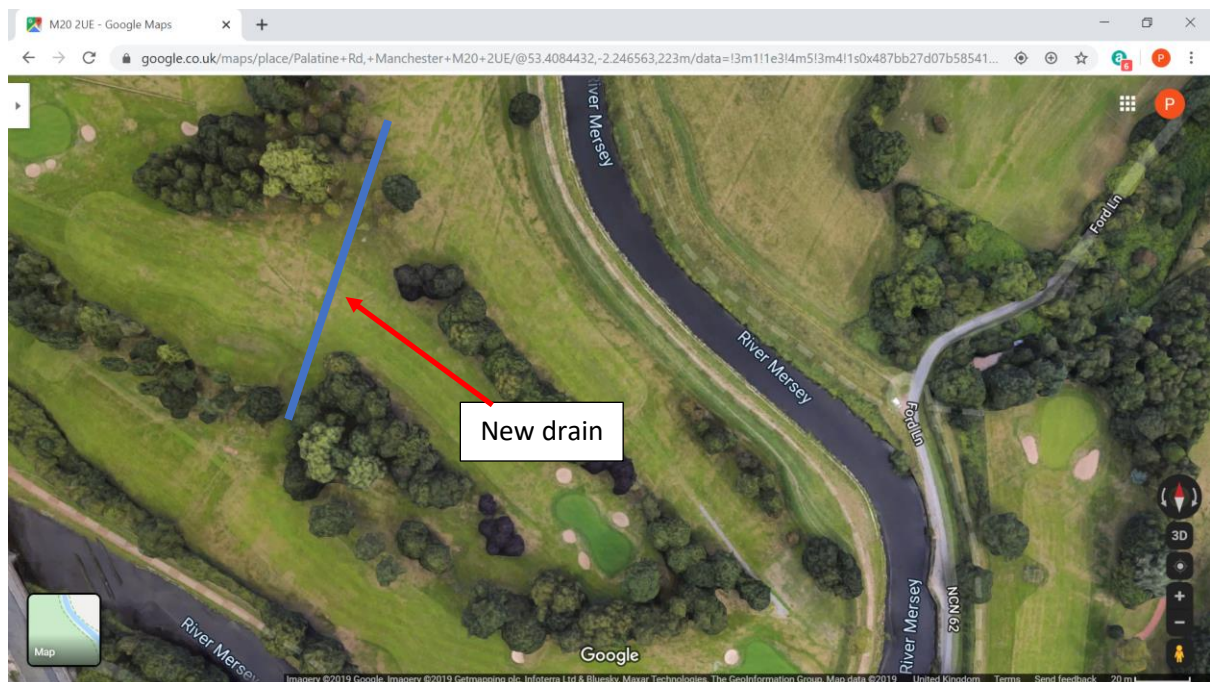

Hole 15

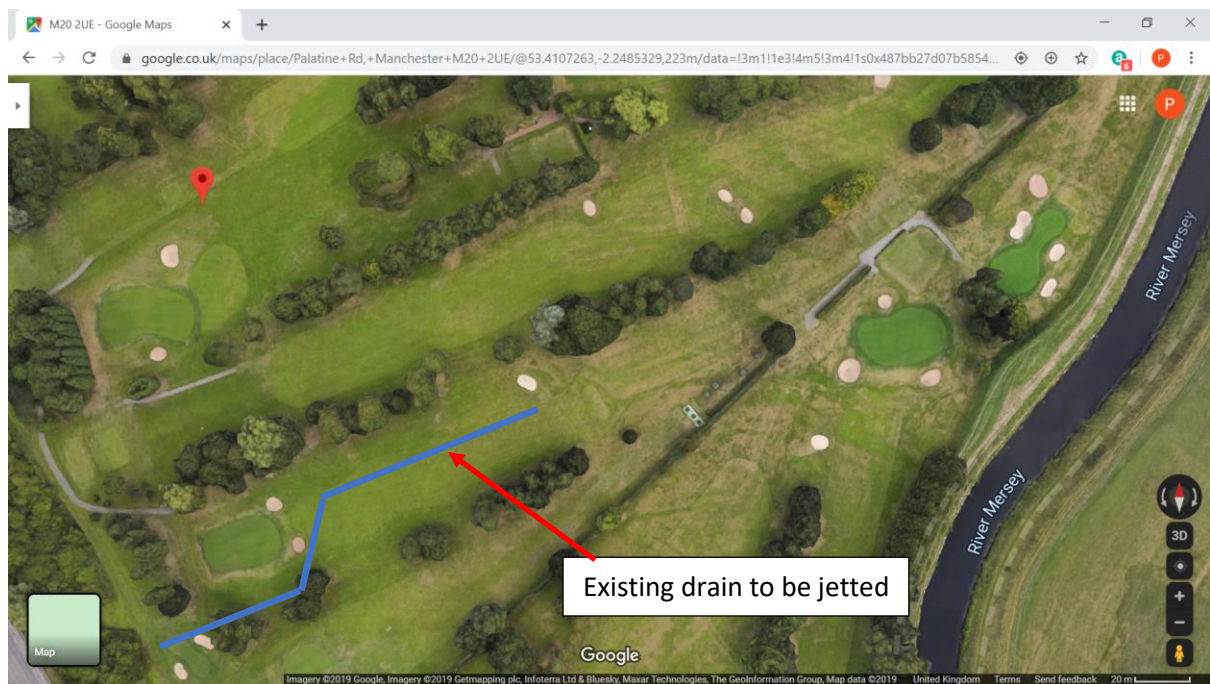

Phase 4

All existing drains to be jetted and cleaned.

Hole 16



Phase 4

Jetting of existing drains

Phase 5 – 2022/2023


Installation of additional drains

Hole 17 and 18

Phase 1 completed

Phase 3

Installation of new pond. Full extent shown when pond is full. During drier periods the pond level will be lower and will have less of an impact on play of the 17th hole. A drain will be installed to connect the new pond with the existing pond adjacent 16th tee.

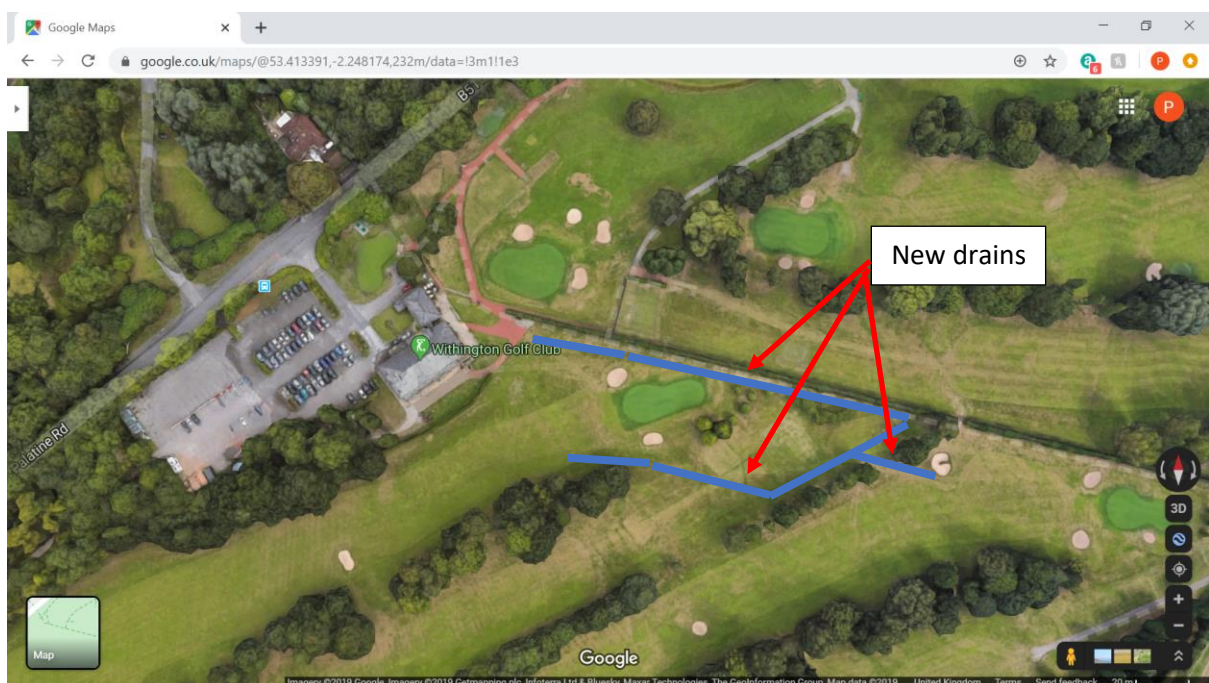

Phase 4

All drains to be jetted and cleaned.

Phase 5

New Drains to be installed.
