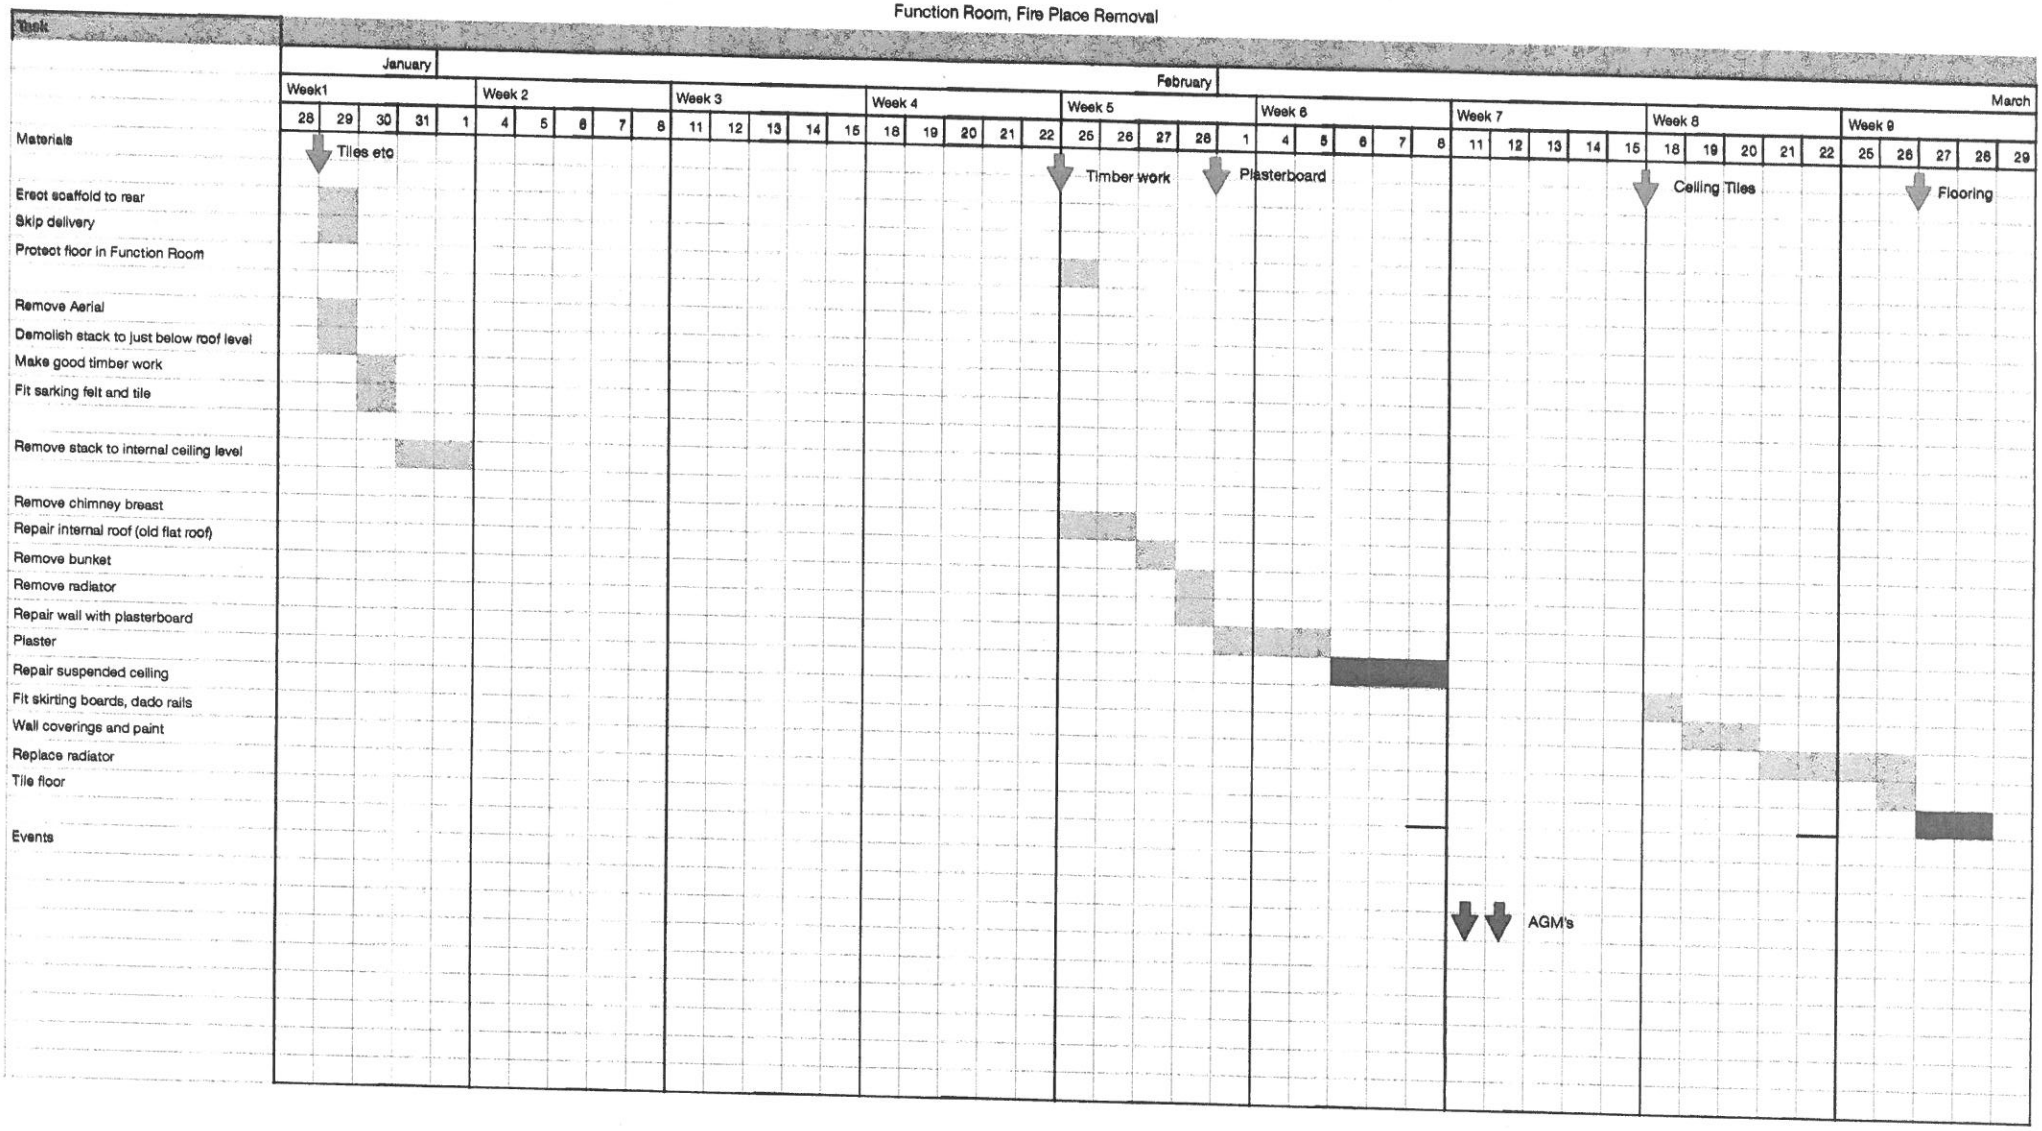
Function Room, Fire Place Removal
Task
January
February
March
Week1
Week 2
Week 3
Week 4
Week 5
Week 6
Week 7
Week 8
Week 9
28 29 30 31 1 4 5 6 7 8 11 12 13 14 15 18 19 20 21 22 25 26 27 28 1 4 5 6 7 8 11 12 13 14 15 18 19 20 21 22 25 26 27 28 29
Materials
Tiles etc
Timber work
Plasterboard
Ceiling Tiles
Flooring
Erect scaffold to rear
Skip delivery
Protect floor in Function Room
Remove Aerial
Demolish stack to just below roof level
Make good timber work
Fit sarking felt and tile
Remove stack to internal ceiling level
Remove chimney breast
Repair internal roof (old flat roof)
Remove bunket
Remove radiator
Repair wall with plasterboard
Plaster
Repair suspended ceiling
Fit skirting boards, dado rails
Wall coverings and paint
Replace radiator
Tile floor
Events
AGM's
